
	(A)	Nombre	Duracion	Inicio	Terminado	Predecesores
1	★!	Analisis y Diseño	24 days	22/01/25 8:00	24/02/25 17:00	
2		Revión de statius	1 day	22/01/25 8:00	22/01/25 17:00	
3		Correcion de error	4 days	23/01/25 8:00	28/01/25 17:00	
4	Ö	Reunión de ajuste	2 days	27/01/25 8:00	28/01/25 17:00	
5	Ö	Creacion de docu	5 days	29/01/25 8:00	04/02/25 17:00	
6	Ö	Realizar diseño det	7 days	30/01/25 8:00	07/02/25 17:00	4
7	Ö	Realizar modelado	6 days	04/02/25 8:00	11/02/25 17:00	
8	Ö	Realizar diseño de	3 days	03/02/25 8:00	05/02/25 17:00	
9	Ö	Verificación del do	1 day	31/01/25 8:00	31/01/25 17:00	
10	Ö	Corrección de defe	1 day	03/02/25 8:00	03/02/25 17:00	
11	Ö	Realizar plan de pr	2 days	12/02/25 8:00	13/02/25 17:00	
1 2	Ö	Verificación de pla	2 days	13/02/25 8:00	14/02/25 17:00	
1 3	Ö	Corrección de erro	1 day	17/02/25 8:00	17/02/25 17:00	
1 4	Ö	Actualizar matriz d	1 day	05/02/25 8:00	05/02/25 17:00	
1 5	Ö	Verificar matriz de	1 day	06/02/25 8:00	06/02/25 17:00	
16	Ö	Corrección de erro	1 day	06/02/25 8:00	06/02/25 17:00	
17	Ö	Elaborar reporte d	1 day	03/02/25 8:00	03/02/25 17:00	
18		Definir Acciones co	1 day	17/02/25 8:00	17/02/25 17:00	
19	Ö	Revisión de plan d	3 days	19/02/25 8:00	21/02/25 17:00	
2 0	Ö	Validación/Aceptac	1 day	24/02/25 8:00	24/02/25 17:00	
2 1		Construccion	60 days	03/03/25 8:00	23/05/25 17:00	
2 2		Reunión para la di	1 day	03/03/25 8:00	03/03/25 17:00	
2 3	Ö	Implementación de	5 days	04/03/25 8:00	10/03/25 17:00	
2 4	Ö	Componentes	54 days	03/03/25 8:00	15/05/25 17:00	
2 5		Programar CU	2 days	03/03/25 8:00	04/03/25 17:00	
26	Ö	Programar login	2 days	03/03/25 8:00	04/03/25 17:00	
27	Ö	Programar CU	2 days	05/03/25 8:00	06/03/25 17:00	
28	Ö	Programar men	2 days	05/03/25 8:00	06/03/25 17:00	
29		Programar CU		07/03/25 8:00	11/03/25 17:00	
3 0	Ö	Programar form		07/03/25 8:00	07/03/25 17:00	
3 1		Programar form		10/03/25 8:00	10/03/25 17:00	
3 2		Programar form		11/03/25 8:00	11/03/25 17:00	
3 3		Programar CU_04		12/03/25 8:00	17/03/25 17:00	
3 4		Programar form		12/03/25 8:00	13/03/25 17:00	

Nombres del Recurso	19 ene 25 D L M M J V
Jose Antonio Huerta Salguero;Oscar Ulises Hernandez Vaquez;Saul Alonso Serrano;Vlctor Meneses Garcia	-
	
SGA - pagina2	,
36A - paymaz	

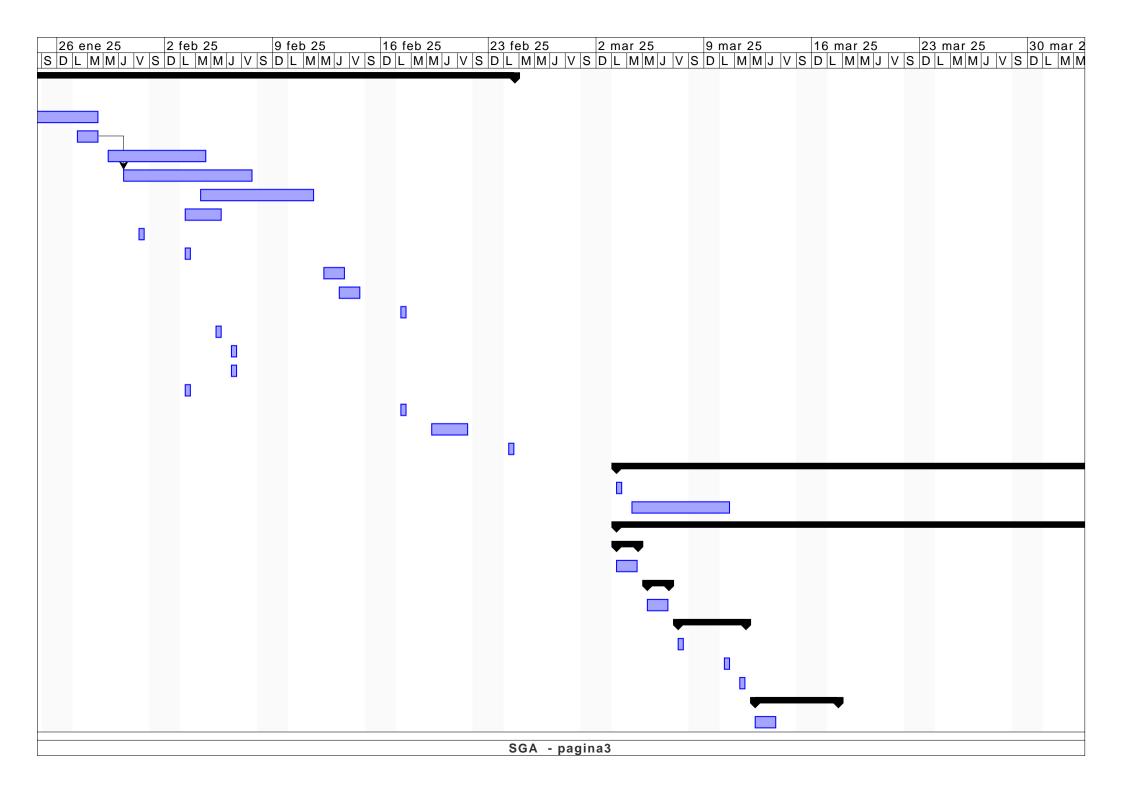



5	6 a	abr 25	13	3 abr 25	20	abr 25	27	abr 25	4	may 25	11	may 25	18	3 may 25	25	may 25	1 jur	n 25	8 ju
JV	S D	L M M J	V S D	abr 25 L M M J V	S D	L MMJ V	S D	L M M J V	S D	L MMJ	/ S D	L MMJ	V S D	L MMJ V	S D	L MMJ V	S D L	MMJ V	S D L
													,						
									SGA	A - pagina	14								

n 25	1	15 jun D L M	25	\ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \	22
MMJ	VSI) L N	1 M J	VS	D
	SGA	- naa	ina5		
	JGA	- pag	iiiab		

	®	Nombre	Duracion	Inicio	Terminado	Predecesores
3 5	Ö	Programar form	2 days	14/03/25 8:00	17/03/25 17:00	
3 6	Ö	Programar CU_05	1 day	17/03/25 8:00	17/03/25 17:00	
3 7	Ö	Programar dos	1 day	17/03/25 8:00	17/03/25 17:00	
3 8	Ö	Programar CU_06	2 days	18/03/25 8:00	19/03/25 17:00	
3 9	Ö	Programar un s	2 days	18/03/25 8:00	19/03/25 17:00	
4 0	Ö	Programar CU_07	2 days	20/03/25 8:00	21/03/25 17:00	
4 1	Ö	Programar un s	2 days	20/03/25 8:00	21/03/25 17:00	
4 2	Ö	Programar CU_08	1 day	24/03/25 8:00	24/03/25 17:00	
4 3	Ö	Programar dos	1 day	24/03/25 8:00	24/03/25 17:00	
4 4	Ö	Programar CU_09	2 days	25/03/25 11:00	27/03/25 11:00	
4 5	Ö	Programar dos	2 days	25/03/25 11:00	27/03/25 11:00	
4 6	Ö	Programar CU_10	6 days	28/03/25 8:00	04/04/25 17:00	
47	Ö	Programar dos	6 days	28/03/25 8:00	04/04/25 17:00	
4 8	Ö	Programar CU_11	2 days	07/04/25 8:00	08/04/25 17:00	
4 9	Ö	Programar dos	2 days	07/04/25 8:00	08/04/25 17:00	
5 0	Ö	Programar CU_12	3 days	09/04/25 8:00	11/04/25 17:00	
5 1	Ö	Programar tres	3 days	09/04/25 8:00	11/04/25 17:00	
5 2	Ö	Programar CU_13	2 days	14/04/25 8:00	15/04/25 17:00	
5 3	Ö	Programar un s	2 days	14/04/25 8:00	15/04/25 17:00	
5 4	Ö	Programar CU_14	3 days	16/04/25 8:00	18/04/25 17:00	
5 5		Programar tres	3 days	16/04/25 8:00	18/04/25 17:00	
5 6		Programar CU_15	3 days	21/04/25 8:00	23/04/25 17:00	
5 7	Ö	Programar tres	3 days	21/04/25 8:00	23/04/25 17:00	
58	Ö	Programar CU_16	3 days	23/04/25 8:00	25/04/25 17:00	
5 9		Programar tres	3 days	23/04/25 8:00	25/04/25 17:00	
6 0	Ö	Programar CU_17	2 days	28/04/25 8:00	29/04/25 17:00	
6 1		Programar tres	2 days	28/04/25 8:00	29/04/25 17:00	
6 2	Ö	Programar CU_18	4 days	30/04/25 8:00	05/05/25 17:00	
6 3		Programar dos	4 days	30/04/25 8:00	05/05/25 17:00	
6 4	Ö	Programar CU_19		05/05/25 8:00	08/05/25 17:00	
6 5		Programar dos	4 days	05/05/25 8:00	08/05/25 17:00	
6 6		Programar CU_20		09/05/25 8:00	09/05/25 17:00	
6 7	•	Programar un s	1 day	09/05/25 8:00	09/05/25 17:00	
68		Programar CU_21		12/05/25 8:00	13/05/25 17:00	

Nombres del Recurso	19 ene 25 D L MMJ V
SGA - pagina7	

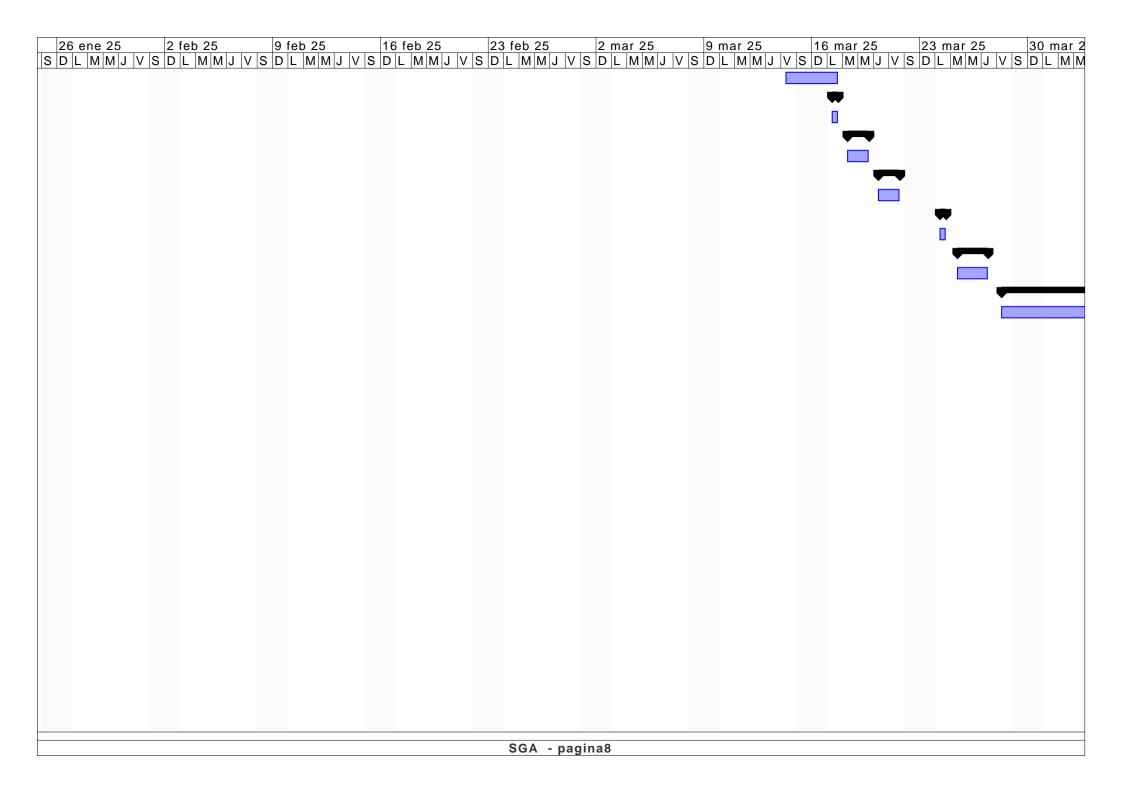


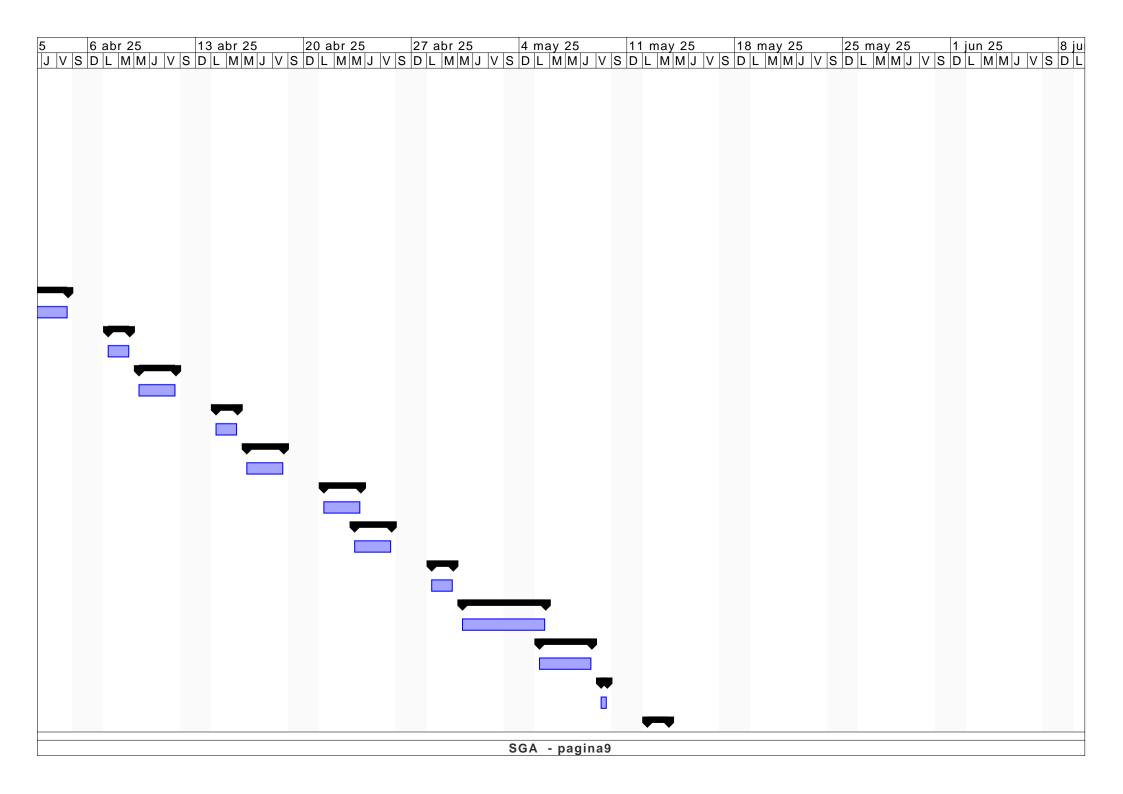


n 25	15	jun 25 L M M J	22
MMJ	V S D	L MMJ	V S D
S	GA -	pagina10)

	(A)	Nombre	Duracion	Inicio	Terminado	Predecesores
6 9	Ö	Programar un s	2 days	12/05/25 8:00	13/05/25 17:00	
7 0		Programar CU_22	2 days	14/05/25 8:00	15/05/25 17:00	
71		Programar dos	2 days	14/05/25 8:00	15/05/25 17:00	
7 2	Ö	Actualizar matriz d	2 days	19/05/25 8:00	20/05/25 17:00	
7 3	Ö	Verificación de la	1 day	21/05/25 8:00	21/05/25 17:00	
7 4	Ö	Corrección de erro	1 day	21/05/25 8:00	21/05/25 17:00	
7 5	Ö	Elaborar Reporte d	1 day	22/05/25 8:00	22/05/25 17:00	
7 6	Ö	Revisión de Plan d	1 day	23/05/25 8:00	23/05/25 17:00	

Nombres del Recurso	19 ene 25 D L M M J V
SGA - pagina12	

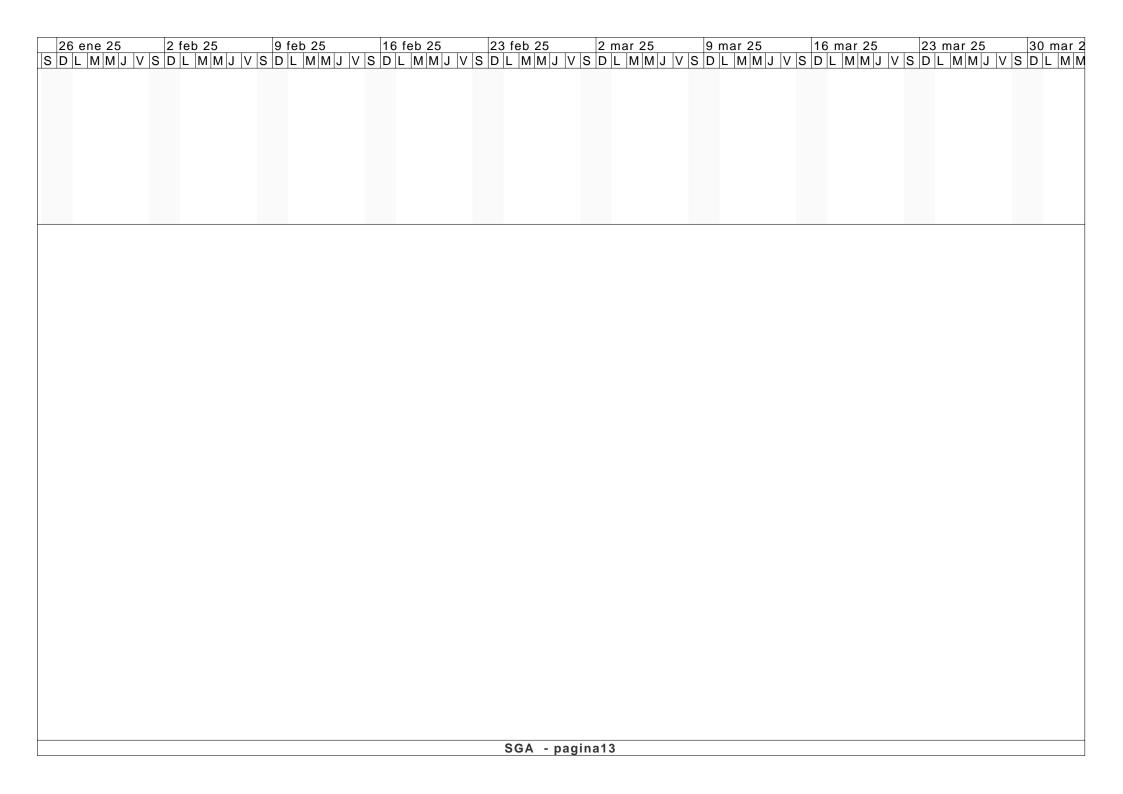

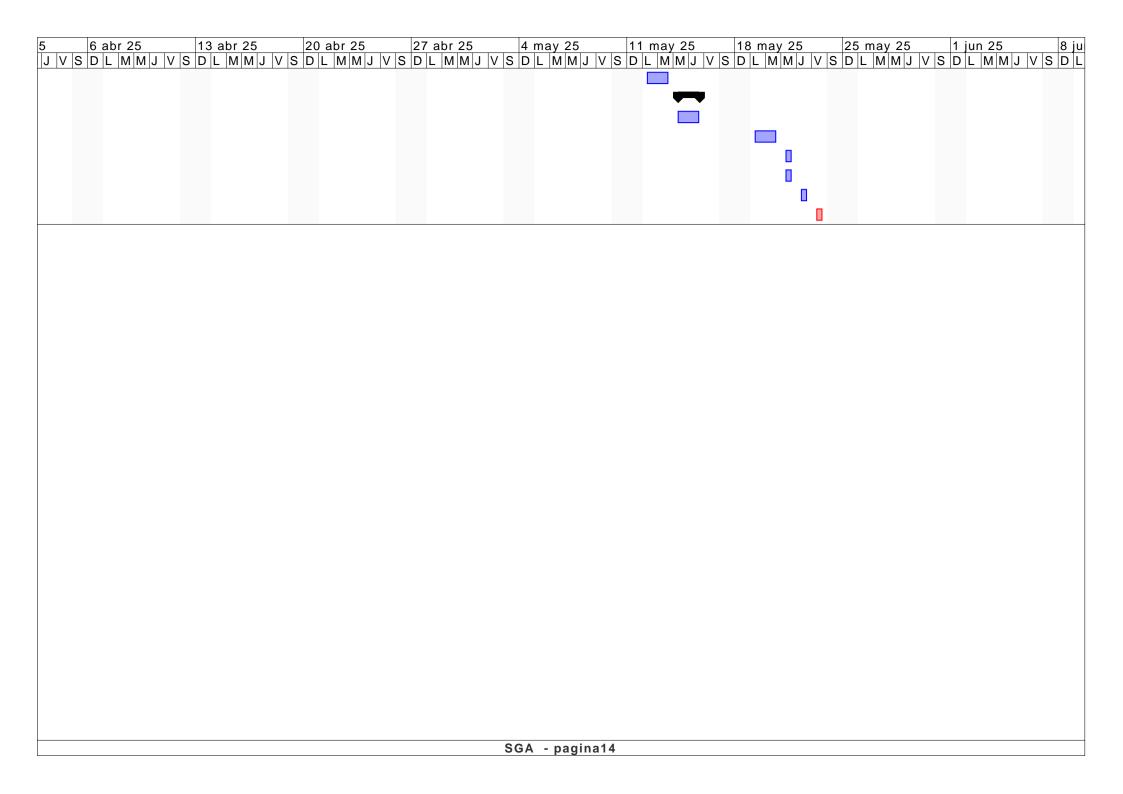

n 25	JV	15 S D	jun L M	25 M J	V	22 S D
11111111				1		
	SG	A -	pagi	na15		
